

PRIMAVERA P6 EPPM

TEAM MEMBER

Team Member Nedir?

- Proje ekibinin sorumlu oldukları işleri görüp, ilerleme ve durum bilgilerini güncelleyebildikleri bir Primavera modülü
- Alternatif kullanım yöntemleri
 - Mobil uygulama
 - P6 Team Member web arayüzü,
 - E-posta servisi

Team Member

Primavera P6 Team Member aracılığıyla,

- Sadece size atanmış işleri görebilir
- İşlerinize gerçekleşen miktarları girebilir
- Ardıl ve öncül işleri görebilir ve o işlere atanmış kaynaklarla iletişim kurabilir
- Proje yöneticisi veya diğer takım üyeleriyle iletişim kurabilir
- Bir işle ilişkilendirilmiş dokümanları görebilir
- Zaman çizelgeleri doldurarak, her bir işte ne kadar çalıştığınızı kayıt altına alabilirsiniz

P6 Team Member Ayarları

Team Member'a giriş yapacak kullanıcılar, Team Member modül erişimi yetkisi ile P6 içerisinde tanımlanır

Users				
Login Name	Personal Name	Resource Access	Global Security Profile	Associated Resource
Project Manager				
Resource Manager				
Status Updater				
ecteamuser	ecteamuser		Status Updater	
Timesheets only				

Module Access	
Module	Access
Contributor	☐
Enterprise Reports	☐
Integration API	☐
P6 Analytics	☐
P6 Professional	☐
Portfolios	☐
Projects	☐
Resources	☐
Team Member	☒
Timesheet	☐
Web Services	☐

Project Access Module Access

P6 Team Member Ayarları

Kullanıcıların hangi alanları güncelleyebileceği proje bazında belirlenir.

The screenshot shows the 'Project Preferences of EC00515' dialog box, specifically the 'Team Member' tab. The left sidebar lists various settings categories: Analytics, Calculations, Contract Management, Defaults, General, Unifier, Services, and Team Member (which is currently selected). The main area of the dialog is divided into two sections: 'Assignment Fields' and 'Activity Fields'. Under 'Assignment Fields', there are two dropdown menus: 'Actual Units' and 'Remaining Units', each with a small 'x' icon to its right. Under 'Activity Fields', there are three dropdown menus: 'Activity % Complete', 'Remaining Duration', and 'Expected Finish', each also with a small 'x' icon to its right. Above these fields, there are radio buttons for 'Resource Assignments', 'Activity Owners/Primary Resources', and 'Both' (which is selected), and a checkbox for 'Include Primary Resources'. Below the fields, there are two checked checkboxes: 'Team members enter new actual units' and 'Team member can status other resource assignments on an activity'. At the bottom, there is a section for 'Select the field team members use to status tasks in Timesheets view' with radio buttons for 'Percent Complete' and 'Remaining Units' (which is selected). The dialog has a 'Help' button at the bottom left and 'Save', 'Save and Close', and 'Cancel' buttons at the bottom right.

Project Preferences of EC00515

Team Member

Status Updates Activity Updates Status Reviews

Team members are assigned to activities as:

☐ Resource Assignments ☐ Activity Owners/Primary Resources ☒ Both ☐ Include Primary Resources

Select the fields team members can update

Note: Actual Start and Actual Finish are always editable. Remaining Early Finish is always editable for assignments.

Assignment Fields +Add

Actual Units x

Remaining Units x

Activity Fields +Add

Activity % Complete x

Remaining Duration x

Expected Finish x

☒ Team members enter new actual units

☒ Team member can status other resource assignments on an activity

Select the field team members use to status tasks in Timesheets view


☐ Percent Complete

☒ Remaining Units

Help Save Save and Close Cancel

P6 Team Member Ayarları

Yapılan
güncellemelerin
onaydan geçip
geçmeyeceği, eğer
onaydan geçecekse
kim tarafından
onaylanacağı
belirlenebilir

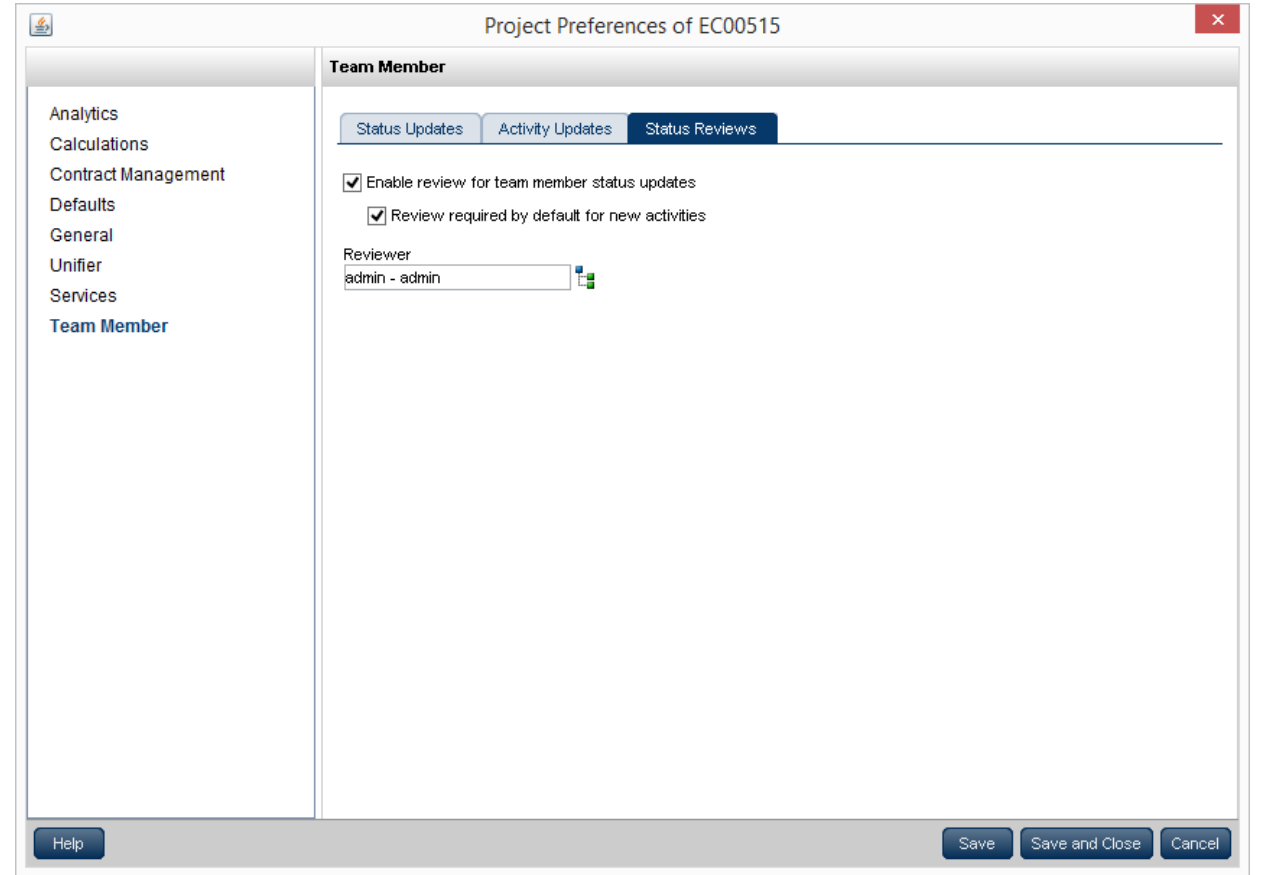

The screenshot shows the 'Project Preferences of EC00515' dialog box. The 'Team Member' tab is selected in the left sidebar. The main area has three sub-tabs: 'Status Updates', 'Activity Updates', and 'Status Reviews'. Under 'Status Reviews', there are two checked options: 'Enable review for team member status updates' and 'Review required by default for new activities'. Below these, the 'Reviewer' field is set to 'admin - admin'. At the bottom, there are buttons for 'Help', 'Save', 'Save and Close', and 'Cancel'.

Project Preferences of EC00515

Team Member

Status Updates Activity Updates Status Reviews

☒ Enable review for team member status updates


☒ Review required by default for new activities

Reviewer
admin - admin

Help Save Save and Close Cancel

Aktivite Sorumlularının Belirlenmesi

Güncelleme yapacak kullanıcılar «Owner» olarak proje pnındaki aktivitelere atanır

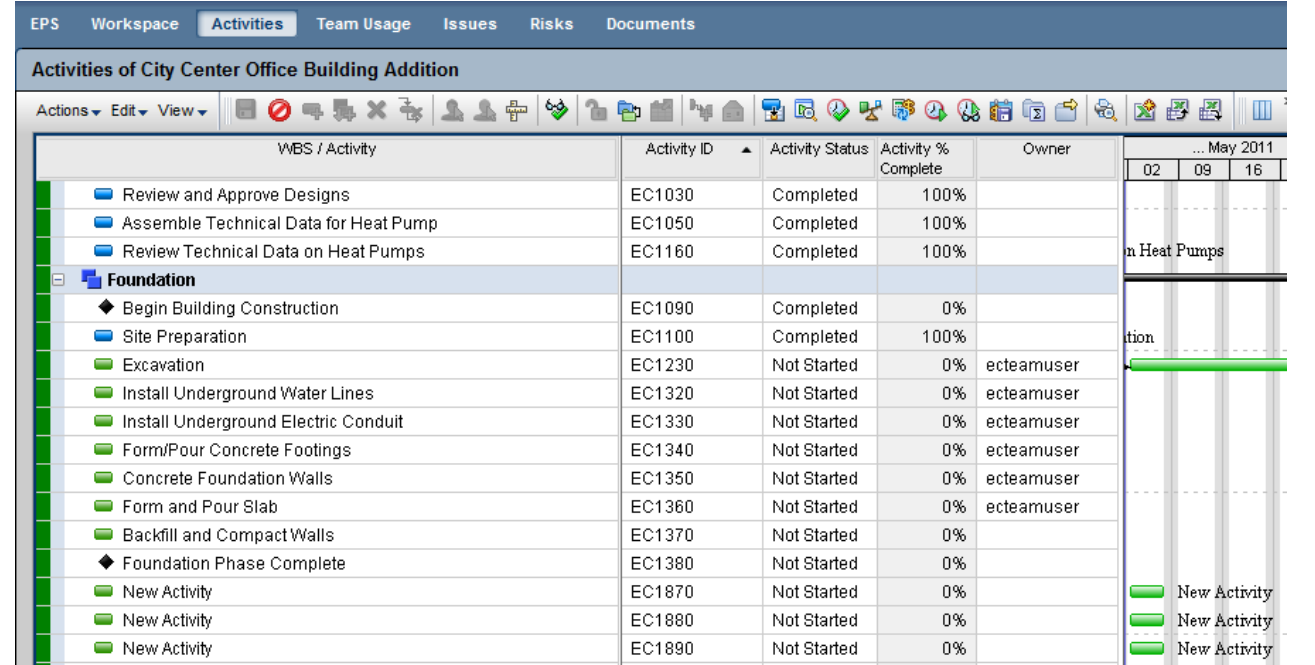

WBS / Activity	Activity ID	Activity Status	Activity % Complete	Owner
Review and Approve Designs	EC1030	Completed	100%	
Assemble Technical Data for Heat Pump	EC1050	Completed	100%	
Review Technical Data on Heat Pumps	EC1160	Completed	100%	
Foundation				
Begin Building Construction	EC1090	Completed	0%	
Site Preparation	EC1100	Completed	100%	
Excavation	EC1230	Not Started	0%	ecteamuser
Install Underground Water Lines	EC1320	Not Started	0%	ecteamuser
Install Underground Electric Conduit	EC1330	Not Started	0%	ecteamuser
Form/Pour Concrete Footings	EC1340	Not Started	0%	ecteamuser
Concrete Foundation Walls	EC1350	Not Started	0%	ecteamuser
Form and Pour Slab	EC1360	Not Started	0%	ecteamuser
Backfill and Compact Walls	EC1370	Not Started	0%	
Foundation Phase Complete	EC1380	Not Started	0%	
New Activity	EC1870	Not Started	0%	
New Activity	EC1880	Not Started	0%	
New Activity	EC1890	Not Started	0%	

Team Member Görünümü

ORACLE PRIMAVERA Team MemberVanessa Lafferty ?

My Tasks Timesheets

My Tasks

Projects All Projects

Status Active

Timeframe All

Resources All Resources

Sort By Finish Date

1 Updates (1) Cancel Save

2

32 tasks found

3 77%
IT1030 - Define Business Requirements *
Project: Zenith Continuity Program
WBS: Requirements Phase
Started: Aug-01-2012
Finish By: Aug-25-2014
4

3 80%
IT1040 - Define System Requirements
Project: Zenith Continuity Program
WBS: Requirements Phase
Started: Sep-04-2014
Finish By: Nov-13-2014

5
IT1030 - Define Business Requirements *
Project: ACH Integration Project
WBS: Requirements Phase
Start By: Sep-22-2014
Finish By: Nov-13-2014
2

6
IT9003 - Gate 2 - Requirements Approved
Project: ERP Legacy Merge
WBS: Key Milestones
Start By:
Finish By: Jan-23-2015

7
* IT1040 - Define System Requirements
Project: ERP Legacy Merge
WBS: Requirements Phase
Documents, Notebooks, Related Tasks
Started: Sep-06-2014
Finish By: Jan-23-2015
8 1

10
IT1040 - Define System Requirements
Project: ERP Legacy Merge
WBS: Requirements Phase
Start By: Oct-30-2014
Finish By: Jan-23-2015
1

4
IT1040 - Define System Requirements

Started
Sep-06-2014

Finish By
Jan-23-2015

% Complete
0

Remaining Duration
61d 4h

Undo Status Other Resources

Steps

Codes and UDFs

Team Member Görünümü

1	Aktivitelerde bir değişiklik yapıldığında görüntülenir.
2	İşleri proje, durum, zaman aralığı ve kaynağa göre filtreleyebilir, sıralamasını değiştirebilir, işler arasında arama yapabilirsiniz.
3	Bir işteki ilerleme grafiksel olarak görüntülenir.
4	İlerleme panelinden seçilen iş için tarih ve çalışılan zamanı güncelleyebilirsiniz.
5	Bir P6 kullanıcısı tarafından projenin kilitlendiğini belirtir. Kilit kaldırılana kadar o aktiviteye güncelleme yapılamaz.
6	İşin kilometre taşı tipinde bir aktivite olduğunu belirtir.


Team Member Görünümü

7	Bir işi seçerek o işin durumunu ilerleme, adım, kodlar ve UDF panellerini kullanarak güncelleyebilirsiniz.
8	Seçilen işe atanmış diğer takım üyeleri ve proje yöneticisiyle devam eden tartışmaları görebilir, e-posta butonu ile bu kişilere e-posta gönderebilirsiniz. Sizin için önemli olan işlere yıldız atayarak ön plana çıkarabilirsiniz. Seçtiğiniz işi tamamlandı olarak işaretleyebilirsiniz.
9	Aktiviteyle ilişkilendirilmiş dokümanları ve not defterlerini inceleyebilirsiniz. Ardıl ve öncül aktivitelerin neler olduğunu görebilirsiniz.
10	Seçilen işi başladı olarak işaretleyebilir, böylece diğer alanların düzenlenebilir hale gelmesini sağlayabilirsiniz.

P6 Mobile Apps

- P6 Team Member mobil uygulamaları, kullanıcıların atandıkları işlere iPad, iPhone veya Android cihazlardan kolaylıkla güncelleme yapabilmelerine olanak tanır.
- Kullanıcılar internet bağlantısı olmadığı durumlarda da çevrimdışı çalışarak aktiviteleri güncelleyebilirler. Böylece yapılan değişiklikler internet bağlantısı sağlandığında otomatik olarak sisteme yansıtılır.
- P6 Team Member mobil uygulamaları aracılığıyla fotoğraf çekip sisteme yükleyebilir, atandığınız bir aktiviteyle çektiğiniz fotoğrafı ilişkilendirebilirsiniz.

iPad Uygulaması

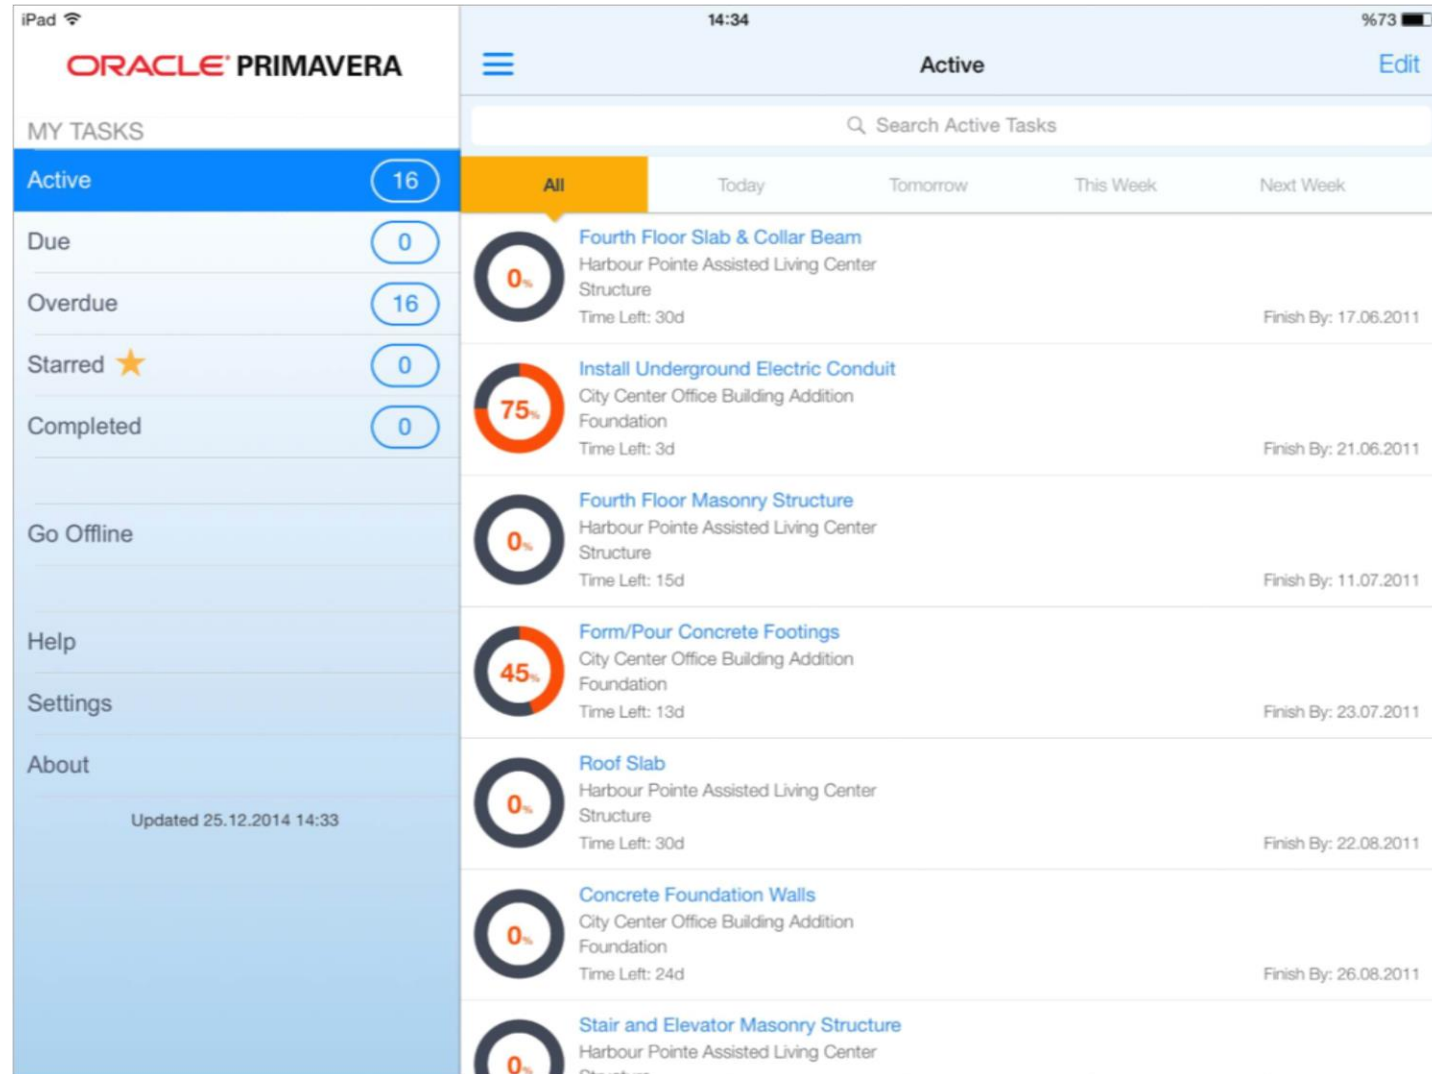

iPhone Uygulaması

Turkcell 14:57 %94

[← Tasks](#) [↩](#) [✉](#) [💬](#) [📷](#)

EC1470 • Concrete Basement Slab ☆

Project City Center Office Building Addition

WBS Structure

[Start](#)

Start By

Mar 1, 2012

Remaining Duration

24d

Codes and UDFs

1 >

Related Tasks

2 >

Steps

0 >

Team Member E-Posta Servisi

From:

To:

Cc:

Subject: Fwd: Your requested P6 tasks

Sent: Thu 3/27/2014 11:38

Here is the list of P6 tasks that you requested.

Tasks matching your filter: active

If your e-mail application supports inline text editing, reply to this e-mail with your task updates. When entering task updates, delete the original value in its entirety before entering an updated value. If the original value is not completely removed, an error may occur when sending a reply message in HTML format.

If your e-mail application does not support inline text editing, then select the [Update this task](#) link to update each individual task.

Project: GIS Interface Project

Assignment

WBS: Key Milestones

Status: Not Started

Star Task(Y/N): N

Start: 02-May-2011 08:00 AM

Finish: 06-May-2011 04:00 PM

Finished(Y/N): N

Time Left: 40h

Remaining Duration: 40h

Time Spent: 0m

[Update this task](#)

Owner

WBS: Key Milestones

Status: Not Started

Star Task(Y/N): N

Start: 02-May-2011 08:00 AM

Finish: 06-May-2011 04:00 PM

Finished(Y/N): N

Time Spent (Nonlabor): 0m

Time Spent (Labor): 0m

Time Left (Labor): 0m


[Update this task](#)

Team Member E-Posta Servisi

- Team Member e-posta servisi
 - Mevcut işlerinizi görüntüleyebileceğiniz bir e-posta isteyebilirsiniz. Dilerseniz listeyi proje, zaman aralığı, durumu, veya yıldızlananlar olarak filtreleyebilirsiniz
- Proje yöneticileri yeni kullanıcılara servisin e-posta adresini ve yönergeleri içeren bir e-posta gönderebilir,
 - Proje ekip üyelerinin cevaplayarak aktivitelere güncelleme girebilecekleri bir durum izleme e-postası gönderebilir

Güncelleme Verilerinin Onayı

Eğer proje ayarlarında, Team Member'da girilen bilgilerin onaydan geçmesi ayarlanmışsa, onaylayacak kişiye bu konuda bir bildirim gider

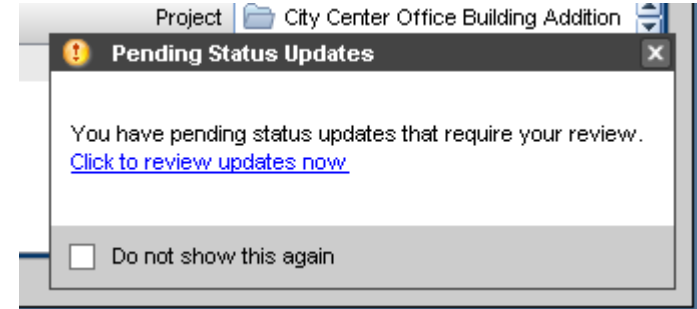

Team Member Onay Aşaması

- P6 içerisinde onay bekleyen güncellemeler görülebilir, aktiviteye ne kadar gerçekleşme girildiği görülerek onaylanır

Review Status Updates

All Open Projects

City Center Office Building Addition

ecteamuser

Excavation

Activity ID: EC1230 Changed Field Old New

Project Name: City Center Offi... Actual Start 02-May-11

Project ID: EC00515 Actual Finish 02-Jun-11

ecteamuser Remaining Duration 23 0

Remaining Labor Units 192 0

Actual Labor Units 0 192

More... Hold Override

Install Underground Water Lines

Activity ID: EC1320 Changed Field Old New

Project Name: City Center Offi... Actual Start 03-Jun-11

Project ID: EC00515 Actual Finish 20-Jun-11

ecteamuser Remaining Duration 12 0

Remaining Labor Units 96 0

Actual Labor Units 0 96

More... Hold Override

Install Underground Electric Conduit

Activity ID: EC1330 Changed Field Old New

Number of updates 4 Ready to accept 4

Accept Accept and Close Close
